
November 21, 2019





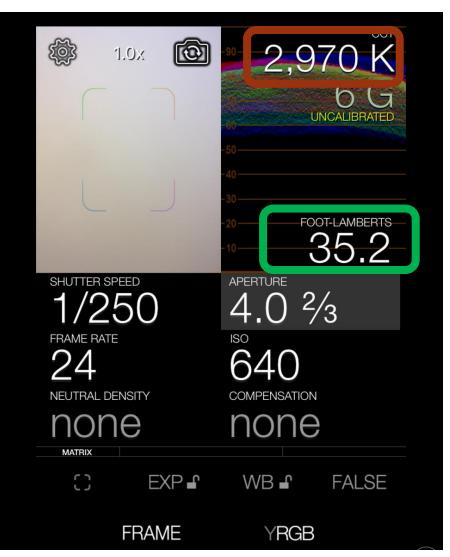

PROPOSITION 39 PROJECT

Contractor crews are finishing the interior lights at the High School and Middle School in the next few weeks. At the same time, District Maintenance crews will be finishing the exterior pole lights.



- Middle School PAC Improvements
 - Installation of a motorized screen and projector has been ordered and will be installed upon arrival.





MIDDLE SCHOOL PLANTER DRAIN

Completed by District maintenance crews.



- Lead Paint Mediation (Adult School Boneyard and Pine Preschool)
 - Completed by District maintenance crews.



Pacific Grove Middle School Cal-Am Grant Landscape Plan



MIDDLE SCHOOL LANDSCAPE PROJECT

Funds for this project are coming from a Cal-Am grant. Completing design and water audit. Project has to be complete before December 15th.



- High School Pool Heater Replacement
 - There will be discussion about replacing both heaters instead of one at this meeting.
 Materials are 3-5 weeks out and replacement will take about two weeks including reheating the pool for use.



- Adult School Outdoor Classroom and Daycare Playground
 - Outdoor classroom is complete and in use. The Daycare playground will begin construction on Nov 25.



QUESTIONS?

